


JTRS Ground Mobile Radios

JTRS GMR · Army · Boeing **CANCELLED**

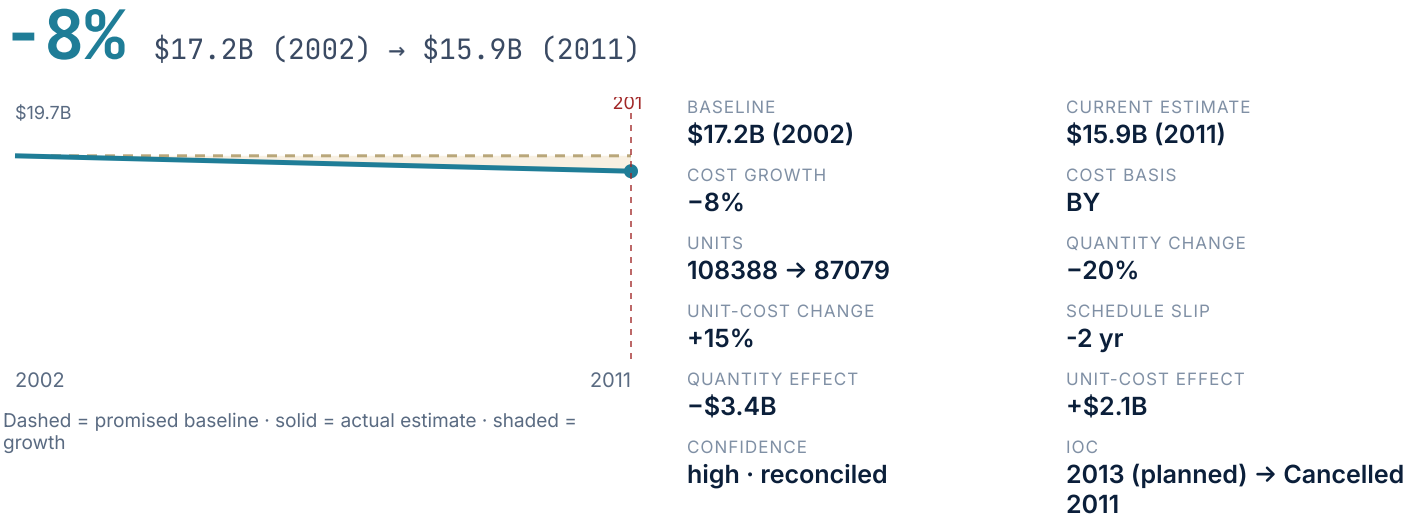

ASSESSMENT

The headline total drifted DOWN — because the buy was shrinking. Development cost grew 69%, the schedule stretched from 55 to 127 months, and after nine years DoD cancelled it before production: the stated post-cancellation total is 90% below the first full estimate, nearly all of it sunk development.

DOCUMENTED EVENTS

2011 Cancelled pre-production

SOURCE

GAO-11-233SP, JTRS GMR profile pp.93-94 — constant FY2011 \$M: first full estimate 06/2002 \$17,164.7M / 108,388 radios vs 01/2011 \$15,867.7M / 87,079; R&D +68.9%, unit cost +15.1%, cycle 55 → 127 months. GAO-13-294SP p.17 + Table 10 p.165: cancelled 2011; post-cancellation total \$1,806M vs \$17,928M first full (FY2013\$), -89.9%.
