


# Land Warrior

Land Warrior · Army · General Dynamics **CANCELLED**

**+30%** \$2.7B (2003) → \$3.5B (2006)

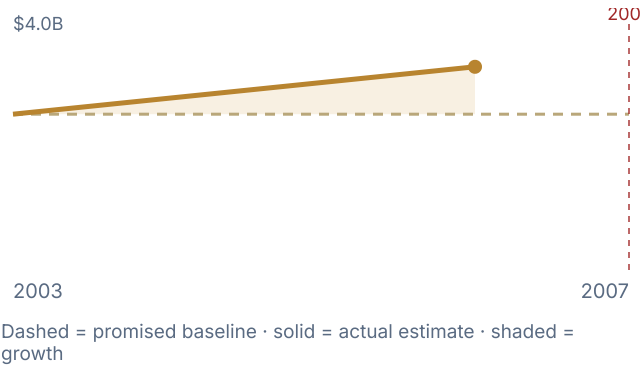

**BASELINE**  
**\$2.7B (2003)**

**COST GROWTH**  
**+30%**

**UNITS**  
**15985 → 24849**

**UNIT-COST CHANGE**  
**-16%**

**QUANTITY EFFECT**  
**+\$1.5B**

**CONFIDENCE**  
**medium · reconciled**

**CURRENT ESTIMATE**  
**\$3.5B (2006)**

**COST BASIS**  
**BY**

**QUANTITY CHANGE**  
**+55%**

**SCHEDULE SLIP**  
**-2 yr**

**UNIT-COST EFFECT**  
**-\$682M**

**IOC**  
**2009 (planned) →**  
**Cancelled 2007**

## ASSESSMENT

Thirteen years, three restructures, and a quantity plan that swung 16,000 → 85,000 → 25,000 before the Army stopped paying in 2007. At the end unit cost was actually 16% BELOW baseline — the program died of shifting scope and budgets, not unit-cost growth. One Stryker battalion took its gear to Iraq anyway. (Confidence medium: the 2003 baseline post-dates two restructures.)

## DOCUMENTED EVENTS

**2007** Cancelled (Army)

## SOURCE

GAO-07-406SP, Land Warrior profile pp.99-100 — constant FY2007 \$M: first full estimate 02/2003 \$2,692.8M / 15,985 systems vs 08/2006 \$3,504.0M / 24,849; unit cost -16.3%; cancellation stated in the same profile. Interim plan swung to 85,412 systems / \$9,274.6M (GAO-06-391, FY2006\$ — different basis, not mixed in). Program start Aug 1994; cycle 145 → 175 months.
