


Columbia-class SSBN

Columbia · Navy · General Dynamics Electric Boat

+9% \$128.0B (2017) → \$139.7B (2023)

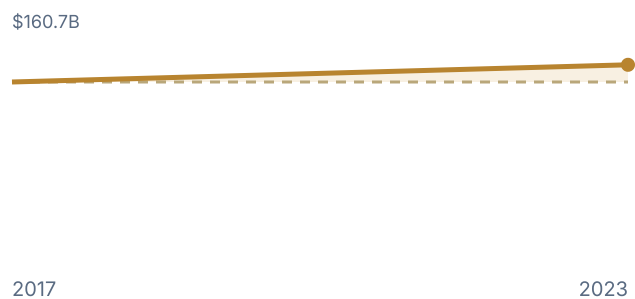

Dashed = promised baseline · solid = actual estimate · shaded = growth

BASELINE
\$128.0B (2017)
COST GROWTH
+9%
UNITS
12 → 12
UNIT-COST CHANGE
+9%
QUANTITY EFFECT
+\$0M
CONFIDENCE
high · reconciled

CURRENT ESTIMATE
\$139.7B (2023)
COST BASIS
TY
QUANTITY CHANGE
0%
SCHEDULE SLIP
0 yr
UNIT-COST EFFECT
+\$11.7B
IOC
2031 → 2031 (first patrol)

ASSESSMENT

+9% like-for-like (then-year). BASIS-MISMATCH TRAP: comparing the \$100B BY2017 baseline to \$139.7B TY overstates growth (~40%); the honest TY-to-TY figure is +9%. Lead-boat schedule under pressure.

SOURCE

CRS [R41129](#) (Dec 2023); Milestone B ADM Jan 2017 (\$128B TY = \$100B BY2017). Dec 2023 MSAR.
